



FINAL PROJECT COMPLETION REPORT

Project Name and Number: 7000 South Utility Project, Phase 1 SD 16-02

Description: Increase storm drain capacity for citizens. This project increased the storm drain system's ability to discharge the 100 year event down to the Jordan River and reduce flooding potential.

Contractor:	Newman Construction	Construction Status:	100%
Original construction contract amount:			\$ 2,535,420.00
Total Change Order amount:			\$ 129,129.25
Current construction contract amount:			\$ 2,664,549.25
Total Change Orders as a percentage of original contract:			5%
Completion schedule:			
Notice to Proceed:			1/29/2016
Final Completion:			7/22/2016

Summary of Change Orders:


Description	Amount
1 Jordan River outfall structure - additional 7 days construction	\$ 24,814.00
2 Larger Rip Rap-additional 3 days construction	\$ 19,685.00
3 Free draining granular backfill	\$ 6,600.00
4 3 trees and beaver cages-additional 1 day of construction	\$ 5,050.00
5 Re-route sanitary sewer-additional 1 day of construction	\$ 14,858.00
6 Materials for underneath junction box-additional 1 day of construction	\$ 5,315.00
7 Additional asphalt by pedestrian bridge	\$ 3,152.00
8 Slurry seal Jordan River Trail parking lot-additional 2 days of construction	\$ 6,210.00
9 Additional secondary waterline	\$ 8,901.00
10 Additional asphalt pavement, base, curb and gutter, sidewalk & stamped concrete	\$ 34,544.25
Total Change Order Amount	\$ 129,129.25

FINAL PROJECT COMPLETION REPORT

Project Name and Number: 7000 South Utility Project, Phase 1 SD 16-02



New pedestrian bridge

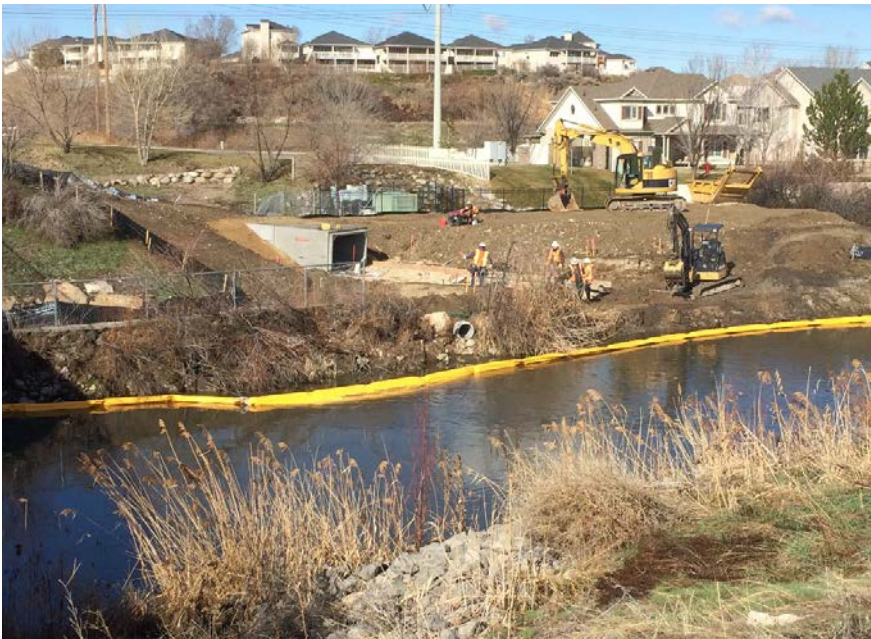

New discharge into the Jordan River
